

Work Order ID 69801

Thursday, May 19, 2011 1:03:46 PM

Page 1

Item ID: D6009-129

Accept

Setup Start

Revision ID:

Stop

Item Name: Crosstube Material

Start Date: 5/19/2011 Start Qty: 40.00

Required Date: 7/12/2012 Req'd Qty: 40.00

Cust Item ID:

Customer:

Reference:

Approvals:

Process Plan: CLDate: 11/05/19

Tooling:

Date:

QC:

Date:

SPC (Y/N):

Date:

Run Start

Stop

Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

Draw Nbr

Revision Nbr

D6009

Rev A

100

0.00



Purchasing

PURCHASING

Purchasing

Memo

Issue P/O:

14138

a) Order as per Dwg D6009

b) Material: 3.500 x 0.625 wall 7075-T6/T6511 (WW-T-700/7 or □QQ-A-225/9 or QQ-A-200/11) seamless aluminum tube

c) Minimum ultimate tensile strength = 77 ksi

d) Minimum tensile yield strength = 66 ksi

e) Tolerance are per ASTM B210 (see details on Dwg D6009)

f) Material certification required

0.00

CL 11/05/19 40

110

Receive & Inspect for Damage & Mat'l Certs

0.00



Packaging

Memo

Ensure material certification is attached

0.00

CL 12/2/12 (43)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 69801

Thursday, May 19, 2011 1:03:46 PM



Item ID: D6009-129

Accept



Setup Start



Revision ID:

Item Name: Crosstube Material

Stop



Start Date: 5/19/2011 Start Qty: 40.00



✓ Cust Item ID:

Required Date: 7/12/2012 Req'd Qty: 40.00



Customer:

Reference:

Run Start



Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Stop



QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Tool ID

Tool #

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

120

QC6- Inspect dimensions to drawing

0.00

81262108

conty
643

QC

Memo

0.00

Quality Control

Ensure Material certification comply to Dwg D6009.

See Dim sheet last page
81262108

140

Identify as per dwg & Stock Location: LG

0.00

Dr 12/02/09

Packaging

Memo

0.00

Packaging

150

QC21- Final Inspection - Work Order Release

0.00

12/2/13

QC

Memo

0.00

Quality Control

10-02-9

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

Page 1

Thursday, May 19, 2011 1:03:43 PM

Work Order ID: 69801

Parent Item: D6009-129

Parent Item Name: Crosstube Material

Start Date: 5/19/2011



Required Date: 7/12/2012

Start Qty: 40.00

Required Qty: 40.00

Comments: IPP Rev:A ☐ 01.08.17 ☐ New Issue ☐ SM
alodine DD 10.01.09 verified by:JLM

IPP Rev:B remove

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D6009-129P  Crosstube Material		Purchased	No			110	Each	0.0000	1 	40		6/12/12 (43)	

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			


NOTE: Date & initial all entries



DESIGN #	DRAWN BY RF	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED #	APPROVED #	DRAWING NO. D6009	REV. A SHEET 1 OF 1
DATE 01.08.16		TITLE CROSSTUBE MATERIAL	SCALE 1:1
A	01.08.16	NEW ISSUE	

SPECIFICATION CONTROL DRAWING

RELEASED
01.08.17 #

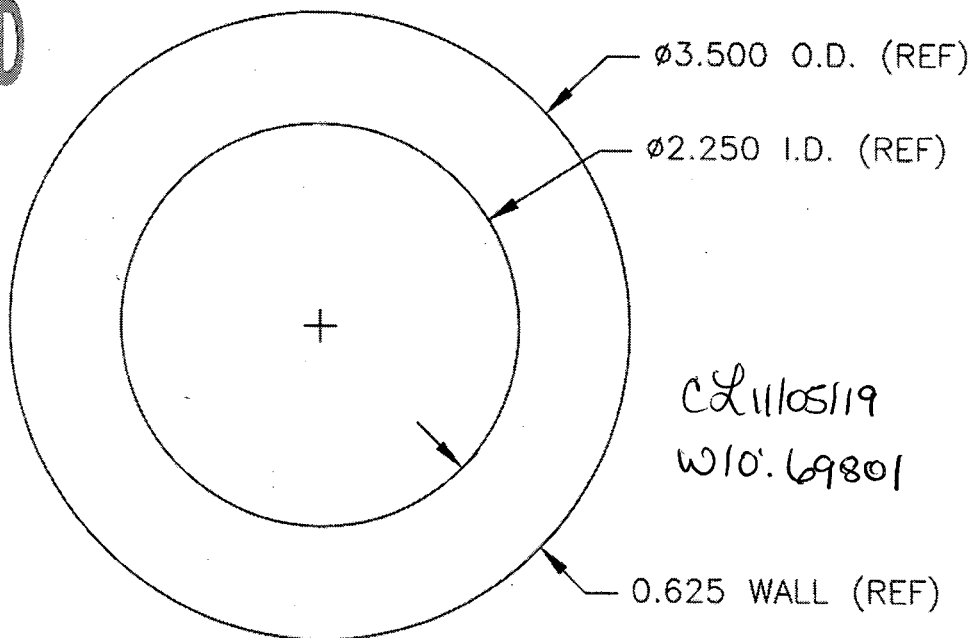

NOTES

- 1) D6009-XXX CROSSTUBE
LENGTH

WHERE XXX IS LENGTH IN INCHES
EG. 129" LONG TUBE: D6009-129

- 2) MATERIAL: 3.500 OD x 0.625 WALL 7075-T6/T6511 (WW-T-700/7 OR QQ-A-225/9 OR QQ-A-200/11) SEAMLESS ALUMINUM TUBE.
MINIMUM ULTIMATE TENSILE STRENGTH = 77 ksi
MINIMUM YIELD TENSILE STRENGTH = 66 ksi
- 3) TOLERANCES ARE PER ASTM B210 AS FOLLOWS:
O.D.: ± 0.008 MEAN (± 0.016 INCLUDING OVALITY)
WALL: ± 0.020 MEAN (± 0.063 INCLUDING ECCENTRICITY)
LENGTH: XXX $+0.188/-0.000$
STRAIGHTNESS: 0.010" DEVIATION / 12" LENGTH
- 4) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.
- 5) CHEMICAL CONVERSION COAT PER DART QSI 005 4.1

Copyright © 2001 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Altima ref. no.	42438/8
Customer P.O.	P.O. 14138
Date:	01.30.12

Dart Aerospace PO. 14138
p6009 - 129
Made in Germany Dest.: Hawkesbury ONT, Canada

free from live plant pests

[illegible]

Abnahmeprüfzeugnis 3.1 - DIN EN 10204:2005

Inspection Certificate 3.1 - DIN EN 10204:2005 / Certificat de Reception 3.1- DIN EN 10204:2005

Kunde: Dart Aerospace Ltd.
Client:

1270 Aberdeen Street
K6A1K7 Hawkesbury, ON Canada

Zeugnisnummer: 100/12

Cert No.: / No. du certificat:

Bestellnummer: PO14138

Order No. / No. de commande

Auftrag: 42438/8

Our Reference/Notre Reference:

Produkt: Rohre nahtlos gepresst
Product / Produit: Tubes seamless extruded

Spezifikation: AMS - QQ - A - 200/11; Spezifikation Dart Aerospace D6009
Specification:

Werkstoff: 7075
Alloy/Alliage:

Zustand: T 6511
Temper/État

Abmessung: 3,500 INCH x 2,250 INCH x 0,625 INCH x 129,000 INCH
Size / Dimension: D6009-129 3.500 X 0.625 X 129

Kennzeichnung: Cert No. 100/12 - ALUnna - 7075 - T6511 - Cast No. 84019 - AMS - QQ - A - 200/11 - 3.500" OD x 0.625" Wall -
Marking/Marquage: Heat Lot No. 1301311 - ALUnna Order Conf No. 42438/8-1 - PO. 14138
Stück kg **Country of Manufacture: Germany**

Lieferung

Delivered Material / Matériel délivré: 43 1446,00 Products are in accordance with applicable RoHS

1. Chemische Analyse

Chemical Analysis / analyse chimique

Elemente ohne Grenzwerte:
einzel max. 0,05 %, insgesamt 0,15 %

Charge/ Cast No.	min.	Si	Fe	Cu	Mn	Mg	Cr	Zn	Ti	Pb	Zr	Bi	Sn	Ni
	max.	0,40	0,50	2,0	0,30	2,9	0,28	6,1	0,20					
84019		0,08	0,17	1,49	0,04	2,38	0,19	5,74	0,04	0,01	0,03			0,0001

Hydrogen content: 0,14

ccm/100 g Al Elements without indication < 0,01 %

country of melt manufacturer: Germany

2. Mechanische Eigenschaften

Mechanical Properties / Valeurs Mécaniques

Anforderungen Requirements	tensile (Rm) ksi	yield (Rp0,2) ksi	elongation 2" %	elongation A %	Hardness HB	Heat Lot No.
min.	77,0	66,0				
max.						
1	83,375	75,980	10,0			1301311
2	71,920	79,895	10,0			
3	83,665	75,835	10,0			
4	87,000	80,620	11,0			

RMS: outside 25 - max. 21,8 µ"

Ergebnis der Prüfungen: Es wird bestätigt, daß die Lieferung geprüft wurde und den Vereinbarungen bei der Bestellannahme entspricht

Test results: We confirm that the delivery has been tested and applies to the agreements made on receipt of the order

Resultats: Nous confirmons que la livraison a été contrôlée et correspond avec les conventions faites à la réception de la commande


31.01.2012 / merg



Certified acc. DIN EN ISO 9001:2008 and DIN EN 9100:2003

valid until 2013-11-10

Cert.- Reg. No.: 001959 QM; 001959 ASH



EXTRUSION INSPECTION SHEET

ULTRA SONIC MEASURMENTS

TUBE #	TOTAL LENGTH	DIA two readings	INSIDE DIA	wall thickness measured w/vern	Straghtness at 12"	Rockwell Reading	LOCATION on tube	R1	R2	R3	R4
1	129.00"	3.495"/3.492"	2.249"	0.612"/0.625"	0.019"	N/A	middle 64.5"	0.631"	0.631"	0.624"	0.624"
2	129.00"	3.500"/3.495"	2.249"	0.612"/0.641"	0.010"	N/A	middle 64.5"	0.630"	0.621"	0.625"	0.632"
3	129.00"	3.490"/3.498"	2.249"	0.615"/0.635"	0.005"	N/A	middle 64.5"	0.633"	0.638"	0.624"	0.618"
4	129.00"	3.491"/3.496"	2.248"	0.623"/0.632"	N/A	N/A	middle 64.5"	0.638"	0.630"	0.616"	0.625"
5	129.00"	3.498"/3.504"	2.250"	0.615"/0.621"	N/A	N/A	middle 64.5"	0.631"	0.624"	0.624"	0.630"
6	129.00"	3.493"/3.494"	2.249"	0.628"/0.612"	N/A	N/A	middle 64.5"	0.621"	0.623"	0.630"	0.623"
7	129.00"	3.491"/3.493"	2.250"	0.616"/0.630"	N/A	N/A	middle 64.5"	0.625"	0.629"	0.627"	0.627"
8	129.00"	3.495"/3.495"	2.249"	0.625"/0.615"	N/A	N/A	middle 64.5"	0.624"	0.623"	0.627"	0.627"
9	129.00"	3.499"/3.498"	2.250"	0.633"/0.613"	0.008"	N/A	middle 64.5"	0.631"	0.641"	0.621"	0.620"
10	129.00"	3.495"/3.501"	2.251"	0.624"/0.618"	N/A	N/A	middle 64.5"	0.619"	0.626"	0.636"	0.637"
11	129.00"	3.497"/3.500"	2.250"	0.625"/0.625"	N/A	N/A	middle 64.5"	0.621"	0.624"	0.632"	0.640"
12	129.00"	3.494"/3.498"	2.252"	0.615"/0.631"	N/A	N/A	middle 64.5"	0.625"	0.629"	0.629"	0.629"
13	129.00"	3.493"/3.495"	2.251"	0.621"/0.615"	N/A	N/A	middle 64.5"	0.631"	0.626"	0.623"	0.628"
14	129.00"	3.491"/3.494"	2.250"	0.620"/0.618"	N/A	N/A	middle 64.5"	0.627"	0.621"	0.626"	0.642"
15	129.00"	3.493"/3.501"	2.246"	0.625"/0.628"	N/A	N/A	middle 64.5"	0.627"	0.630"	0.631"	06.26"
PART # D6009-129		P/O# 14138		BATCH # B69801		Notes:					

5/26/08
